

# Chapter 8: Implementation of the Long-Term Plan for Achieving Water Quality Goals in the Everglades Protection Area

Tracey T. Piccone and Gary F. Goforth

---

## SUMMARY

---

This chapter presents an update on the progress of the implementation of the Long-Term Plan for Achieving Water Quality Goals in the Everglades Protection Area (Long-Term Plan) (Burns and McDonnell, 2003). Because there is overlap between many of the Long-Term Plan projects and other South Florida Water Management District (SFWMD or District) Everglades restoration efforts, the updates for many of the Long-Term Plan projects will appear in other chapters of the *2005 South Florida Environmental Report – Volume I*. For example, the Long-Term Plan projects that cover the Everglades Stormwater Program (ESP) basins and source controls will be covered in Chapter 3 of this volume, and the Long-Term Plan projects relating to the Everglades Construction Project (ECP) Stormwater Treatment Areas (STAs) will be covered in Chapter 4 of this volume. For additional reference, **Table 8-1** indicates the chapter where each Long-Term Plan project update appears.

The long-term Everglades water quality goal is for all discharges to the Everglades Protection Area (EPA) to achieve and maintain water quality standards in the EPA, including compliance with the total phosphorus (TP) criterion established in Rule 62-302.540, Florida Administrative Code (F.A.C.). Substantial progress toward reducing phosphorus levels discharged into the EPA has been made by the State of Florida and other stakeholders. As of April 2004, the Everglades Agricultural Area's (EAA's) Best Management Practices and the Stormwater Treatment Areas combined have removed over 1,730 metric tons of TP that otherwise would have entered the Everglades. Approximately 230 additional metric tons of TP were removed during Water Year 2004 (WY2004) (May 1, 2003 through April 30, 2004), but additional measures are necessary to achieve the Everglades water quality goal. The Long-Term Plan contains activities to achieve that goal, and permits the State of Florida and the District to fulfill their obligations under both the Everglades Forever Act (EFA) [Section 373.4592, Florida Statutes (F.S.)] and the federal Settlement Agreement (Case No. 88-1886-CIV-MORENO). A summarized list and locations of the basins addressed in the Long-Term Plan are presented in **Table 8-2** and **Figure 8-1**, respectively.

The District began implementing the Long-Term Plan projects in Fiscal Year 2004 (FY2004) (October 1, 2003 through September 30, 2004). The Long-Term Plan was submitted to the Florida Department of Environmental Protection (FDEP) in December 2003 as part of the long-term permit application required by the EFA. The first annual public meeting for the Long-Term Plan was held on February 26, 2004 at the District's headquarters in West Palm Beach, Florida.

The District's first request for a minor revision to the Long-Term Plan was approved by the FDEP on April 15, 2004. A description of this minor revision is included in this chapter.

**Table 8-1.** Summary of projects and reference chapters in the Long-Term Plan.

Project Code	Project Description	Chapter References in the 2005 SFER – Volume I
<b><u>Everglades Construction Project (ECP) BASINS</u></b>		
Bc10	Stormwater Treatment Area 1E (STA-1E) Enhancements	4 (STA-1E section)
Bc20	STA-1W Enhancements	4 (STA-1W section)
Bc30	STA-2 Enhancements	4 (STA-2 section)
Bc40	STA-3/4 Enhancements	4 (STA-3/4 section)
Bc50	STA-5 Enhancements	4 (STA-5 section)
Bc60	STA-6 Enhancements	4 (STA-6 section)
Bf	ECP Operation and Maintenance - STAs and non-STAs	4 (each STA section)
Bf80	ECP Compliance Monitoring	4 (each STA section)
Bc05	ECP Operations Monitoring	4 (project-level activities section)
Bf81	STA Site Management	4 (each STA section)
<b><u>Everglades Stormwater Program (ESP) BASINS</u></b>		
Bc75	Acme Basin B	3 (Section II)
Bc71	North Springs Improvement District (NSID)	3 (Section II)
Bc72	North New River Canal (NNRC) Basin	3 (Section II)
Bc73	C-11 West Basin	3 (Section II)
Bc74	Feeder Canal Basin	3 (Section II)
<b><u>PROCESS DEVELOPMENT AND ENGINEERING (PDE)</u></b>		
<b><u>Basin Source Controls</u></b>		
Bc81(1)	EAA Basins - Source Controls	3 (Section I)
Bc81(2)	C-139 Basin - Source Controls	3 (Section I)
<b><u>Enhanced Control and Monitoring</u></b>		
Bc82(1)	Acquisition of Survey Data	4 (project-level activities section)
Bc82(2)	Additional Flow and Water Quality Monitoring Stations	4 (project-level activities section)
Bc82(3)	Review and Correction of Flow Measurement Anomalies	4 (project-level activities section)
Bc82(4)	Analysis and Interpretation	4 (project-level activities section)
Bc82(5)	Update and Maintenance of Hydraulic Models	4 (project-level activities section)
<b><u>Improved Analytical and Forecasting Tools</u></b>		
Bc83(1)	Continued Development and Refinement of Dynamic Model for Stormwater Treatment Areas (DMSTA)	8
Bc83(2)	Water Quality Impacts of Reservoirs	8
Bc83(3)	PSTA Investigations	4 (project-level activities section)
Bc83(4)	PSTA Demonstration Project in STA-3/4	4 (STA-3/4 section)
<b><u>Optimizing SAV Performance</u></b>		
Bc84(1)	Operational Strategy	4 (STA-2 section)
Bc84(2)	Vegetation Maintenance	4 (STA-2 section)
Bc84(3)	Hydrologic and Hydraulic Assessment	4 (STA-2 section)
Bc84(4)	Internal Measurements	4 (STA-2 section)
Bc84(5)	Comparative Analysis	4 (future reports)
<b><u>Additional Structural and Operational Measures</u></b>		
Bc25	Evaluation of Full-Scale STA Enhancements	4 (STA-1W section)
<b><u>Improved Reliability of Inflow Forecasts</u></b>		
Bc86(1)	Update Baseline Data Sets	8
Bc86(2)	Basins With Limited Current Data	8
Bc86(3)	Influence of Comprehensive Everglades Restoration Plan (CERP) Projects on Inflow Volumes and Loads	8
Bc86(4)	Lake Okeechobee Long-term Trends	8
Bc86(5)	Determine Water Quality Relationships in the Everglades Protection Area (EPA)	2C
<b><u>ACCELERATE RECOVERY OF IMPACTED AREAS</u></b>		
Bc87(1)	Recovery Model Development and Calibration	6
Bc87(2)	Downstream Influence of Adding Clean Water to Previously Impacted Areas	6
Bc87(3)	Options for Accelerating Recovery	6
Bc87(4)	Alternatives Analysis and Plan Formulation	6
Bc87(5)	Hydropattern Restoration	6
Bc87(6)	Implement Steps for Recovery in Impacted Areas	6
<b><u>Bc88</u></b>	<b><u>Adaptive Implementation</u></b>	8
<b><u>Bc90</u></b>	<b><u>Program Management</u></b>	8

**Table 8-2.** Everglades Protection Area (EPA) tributary basins included in the Long-Term Plan.

<b>Basin</b>	<b>Canal</b>	<b>Stormwater Treatment Areas (STAs)</b>	<b>Receiving Water Conservation Areas (WCAs)</b>
S-5A (EAA)	West Palm Beach Canal	STA-1W, STA-1E, STA-2	WCA-1
S-6 (EAA)	Hillsboro Canal	STA-2	WCA-2A
S-7 (EAA)	North New River Canal (NNRC)	STA-3/4	WCA-3A
S-8 (EAA)	Miami Canal	STA-3/4, STA-6	WCA-3A
C-51 West and L-8 Basin	C-51 West	STA-1E, STA-1W	WCA-1
C-139 (including Annex)	L-3 canal	STA-5, STA-6	WCA-3A
ACME Basin B	N/A	N/A	WCA-1
North Springs Improvement District (NSID)	N/A	N/A	WCA-2A
North New River Canal (NNRC) (G-123)	NNRC	N/A	WCA-3A
C-11 West	C-11 West	N/A	WCA-3A
Feeder Canal	L-28 interceptor canal	N/A	WCA-3A
L-28	L-28	N/A	WCA-3A

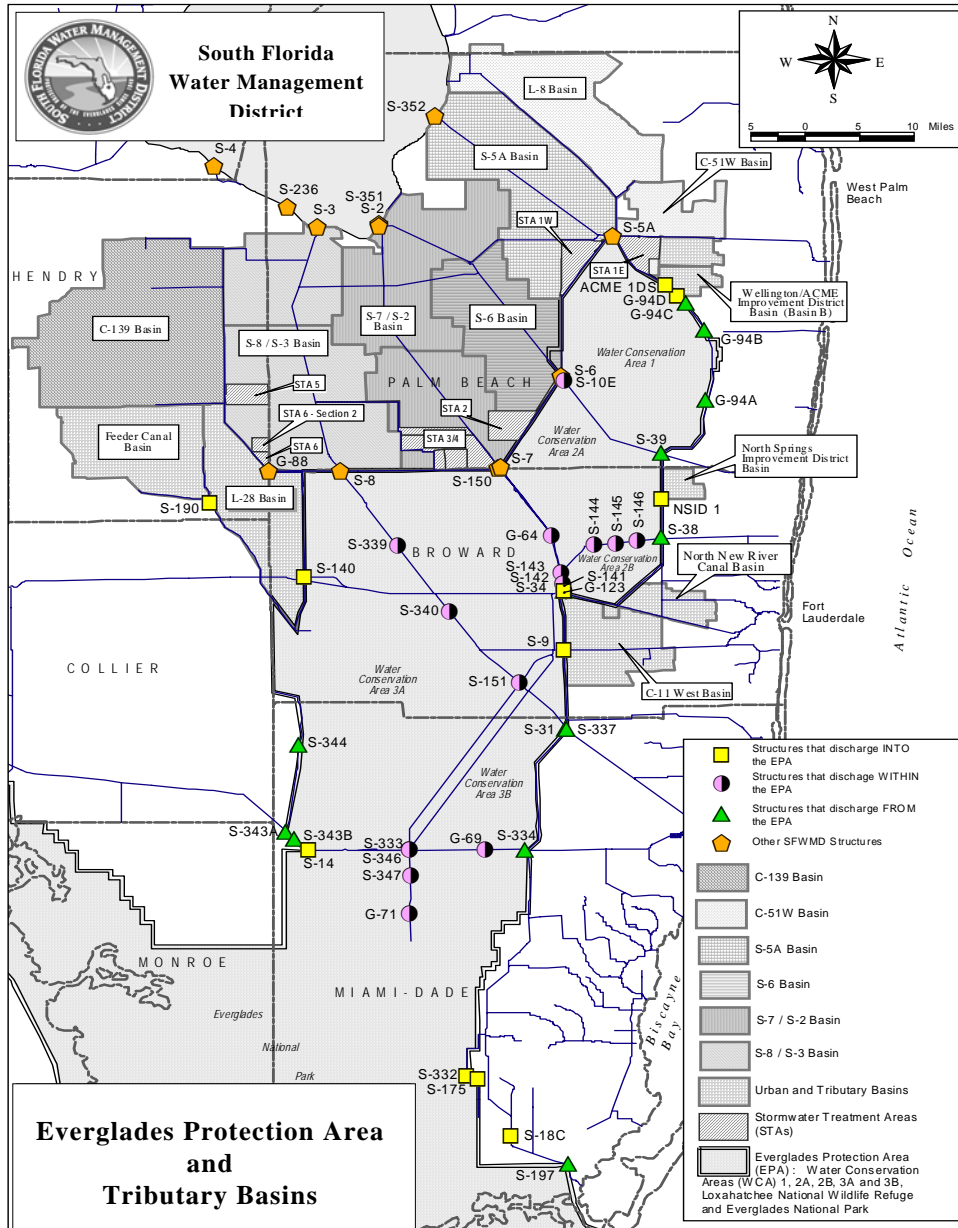


Figure 8-1. Overview of the EPA and tributary basins.

---

## INTRODUCTION

---

The long-term Everglades water quality goal is for all discharges to the Everglades Protection Area (EPA) to achieve and maintain water quality standards, including compliance with the phosphorus criterion established in Rule 62-302.540, Florida Administrative Code (F.A.C.). Substantial progress towards reducing phosphorus levels discharged into the EPA has been made by the State of Florida and other stakeholders. The combined performance of the source controls in the Everglades Agricultural Area (EAA) and the Stormwater Treatment Areas (STAs) of the Everglades Construction Project (ECP) has exceeded expectations. In addition, some source control measures have been implemented in urban and other tributary basins included in the Everglades Stormwater Program (ESP). Nonetheless, additional measures are necessary to achieve the Everglades water quality goal. Technical representatives of the South Florida Water Management District (SFWMD or District), the Florida Department of Environmental Protection (FDEP), the EAA Environmental Protection District (EPD), and other stakeholders used the results of the Basin-Specific Feasibility Studies to formulate a consensus approach to achieving the long-term water quality goals of the Everglades Forever Act (EFA). That recommended approach was set forth in the Long-Term Plan for Achieving Water Quality Goals in the Everglades Protection Area (Long-Term Plan).

The Long-Term Plan contains activities to achieve that goal and to permit the State of Florida and the District to fulfill their obligations under both the EFA [Section 373.4592, Florida Statutes (F.S.)] and the federal Everglades Settlement Agreement (i.e., Settlement Agreement dated July 26, 1991, entered in Case No. 88-1886-CIV-MORENO, U.S. District Court for the Southern District of Florida, as modified by the Omnibus Order entered in the case on April 27, 2001). The Long-Term Plan was developed in full recognition of the substantive remaining scientific uncertainties surrounding that objective. It is predicated upon maximizing water quality improvement through an adaptive implementation process.

---

## OVERVIEW OF THE LONG-TERM PLAN

---

The Long-Term Plan has three primary components:

1. **Pre-2006 Projects:** Structural and operational modifications that can be supported by the current scientific and engineering knowledge base, to be implemented where feasible by December 31, 2006, as well as operation, maintenance, and monitoring of the STAs. The pre-2006 recommended improvements and strategies are considered to be the maximum scientifically defensible steps that had been identified at the time the plan was developed. There is a possibility that these steps will meet a planning target of a long-term, geometric mean total phosphorus (TP) concentration of 10 parts per billion (ppb) in discharges from the various basins. However, it is also possible that these improvements and strategies will not, in and of themselves, provide adequate assurance of an ability to consistently meet that objective on a long-term basis. Therefore, the post-2006 strategy is included in the Long-Term Plan, as discussed below.
2. **Process Development and Engineering (PDE):** Process Development and Engineering (PDE) activities have been designed to (1) further understand and optimize water quality performance in existing and proposed facilities; (2) facilitate integration with the Comprehensive Everglades Restoration Plan (CERP); (3) maintain and improve upon the contribution of source controls to overall water quality improvement goals; and (4)

investigate ways to accelerate the recovery of previously impacted areas in the EPA. Data collected in the PDE will be used to improve the projects contained within the Long-Term Plan, as well as to form the basis for additional projects that may be required to achieve compliance with water quality standards.

3. **Post-2006 Strategy:** The post-2006 strategy will include the identification and adaptive implementation of additional water quality improvement measures that may be considered necessary to comply with water quality standards following completion of the pre-2006 activities, based on ongoing analysis of the PDE effort. It also comprises implementation of steps identified that are capable of accelerating the recovery of previously impacted areas in the EPA, including final implementation of the hydropattern restoration activities directed by the EFA once water quality standards (including the phosphorus criterion) are achieved.

The Long-Term Plan was developed in recognition that:

Achieving water quality standards, including the numeric TP criterion (Rule 62-302.540, F.A.C.) will involve an adaptive management approach, in which the best available information is used to develop and expeditiously implement incremental improvement measures consistent with informed and prudent expenditure of public and private funds.

Continued investigations are necessary to further improve the overall operation and performance of integrated water quality improvement strategies.

Significant performance and economic benefits can be realized by integrating Everglades water quality improvement measures with CERP projects, even to the extent that existing schedules should be reevaluated in some basins and synchronized with CERP project schedules. Modifications to the design and operation of planned CERP projects should be considered.

The Long-Term Plan (dated October 27, 2003) was submitted to the FDEP in December 2003 as part of the long-term permit application required by the EFA. The October 27, 2003 version of the Long-Term Plan is located online on the District's Website at <http://www.sfwmd.gov/org/erd/bsfboard/waterquality.pdf>. Additional information on the Long-Term Plan, including related links, documents, presentations, and photos, can be online found at <http://www.sfwmd.gov/org/erd/longtermplan/index.shtml>.

The Basin-Specific Feasibility Studies, which formed the basis for the Long-Term Plan, are documented in the Evaluation of Alternatives for the ECP Basins (Burns & McDonnell, 2002) and the Basin-Specific Feasibility Studies, Everglades Stormwater Program Basins (Brown & Caldwell, 2002). The feasibility studies are also discussed in Chapter 8A of the 2003 and 2004 Everglades Consolidated Reports. Documents, presentations, data, and other related information on the Basin-Specific Feasibility Studies can be found on the District's Website at <http://www.sfwmd.gov/org/erd/bsfboard/bsfsboard.htm>.

## STATUS OF PROJECT-LEVEL ACTIVITIES

The District began implementing the Long-Term Plan projects in Fiscal Year 2004 (FY2004). The first annual public meeting was held on February 26, 2004 at the District's headquarters in West Palm Beach, Florida. The purpose of this meeting was to update the public on the status of the projects midway through the first year of implementation, and to receive input from the public on proposed modifications to the Long-Term Plan.

Because there is overlap between many of the Long-Term Plan projects and other Everglades restoration efforts by the District, updates for several of the Long-Term Plan projects will appear in other chapters of the *2005 South Florida Environmental Report – Volume I*. **Table 8-1** summarizes all of the Long-Term Plan projects, including cross-references to other chapters in which the specific project update appears. An update on the status of project-level activities for eight of the Long-Term Plan projects for FY2004 is summarized below.

### **Continued Development and Refinement of the Dynamic Model Stormwater Treatment Areas**

The Dynamic Model for Stormwater Treatment Areas (DMSTA) (Walker and Kadlec, 2002) is the tool used to model the future phosphorus performance of the STAs. The DMSTA was used to evaluate components of the Long-Term Plan and will be applied to future enhancements and the interaction between the CERP reservoirs and the STAs. To increase the certainty in the accuracy of the model predictions, the model will be updated and calibrated. Refinements to the DMSTA include calibrating the model using large-scale systems operating in the event-driven mode (e.g., recent STA data), as well as the addition of model compartments, such as a reservoir module, sediment compartment and P speciation components. The tasks identified in the Long-Term Plan for FY2004 are being completed by the U.S. Department of the Interior (USDOI) and the U.S. Army Corps of Engineers (USACE) through contracts with Dr. William W. Walker, Jr. Additional information on the DMSTA can be found online at <http://www.wwwalker.net/dmsta/index.htm>.

### **Water Quality Impacts of Reservoirs**

The Water Quality Impacts of Reservoirs project was initiated in FY2004 as recommended in Section 5.3.2, Water Quality Impacts of Reservoirs of the PDE component of the Long-Term Plan. Because some of the STAs will receive discharges from CERP reservoirs, the primary objective of this project is to assist CERP's Project Delivery Teams (PDTs) in the acquisition and analysis of calibration data sets for use with a water quality model capable of simulating reservoirs. This project is currently contracted with Burns & McDonnell. The contract was executed on November 10, 2003, covering a period of 12 months.

There are three major tasks associated with this contract. The first task, involving identification of data sites and data acquisition, is complete. Thirty-six primary data sites were identified, and various types of data were acquired from three Water Management Districts in Florida. These data include the physical characteristics of the water bodies, time series and non-time series hydrologic and hydraulic data, time series water quality data, non-time series biological data, time-series atmospheric data, and cost information. In order to be useful as a calibration data set, the 36 primary data sites were rated as good, fair, and poor based on the data selection criteria developed by the project team. As a result, eight data sites were rated as good and selected for further analysis. The second task involves the data analysis for the eight selected data sites; this task is near completion. The final task is transformation of the data for use in calibration of a reservoir water quality model such as the DMSTA. This task is scheduled to be completed in early FY2005. This project is currently within budget and on schedule.

### **Update Baseline Data Sets**

As recommended in the Long-Term Plan, the analyses presented in the baseline data for the Basin-Specific Feasibility Studies to Achieve the Long-Term Water Quality Goals for the



Everglades (Goforth and Piccone, 2001) should be updated no less frequently than once every two years to continually improve the degree of confidence in the projected TP loads in inflows to the treatment areas, or in some instances, in discharges directly to the EPA. The Baseline Data report employed available flow and water quality data from 1989–1999; in some basins, little data was available at that time. The first update was initiated by the District in FY2004, and was amended to include the record flow and water quality data through April 30, 2003. A revised ECP base run using the latest version of the South Florida Water Management Model (SFWMM) was also initiated in FY2004 to reflect the latest calibration data for EAA runoff, and to incorporate the latest ECP design information. During the remainder of FY2004 and into FY2005, new regression relationships between the amended historic flow and water quality data will be developed and combined with the results of the ECP base run to develop new 36-year inflow data sets. These data sets can then be used to update the projected TP loads in inflows to the STAs or to the EPA. It is anticipated that this analysis will occur in FY2005, consistent with the Long-Term Plan recommendation to provide funding for the inflow data set updates beginning in FY2005, and extending through FY2015 in alternating years. The District has the responsibility for updating the baseline data sets; the updated data sets are reviewed by the FDEP as well as interested stakeholders.

### **Basins with Limited Current Data**

Water quality performance projections for Everglades restoration efforts depend on understanding water movement and nutrient loadings from multiple watersheds. The projections utilize models that are calibrated from flow and water quality data collected at representative sites throughout the region. After the Everglades Protection Project Conceptual Design (Burns & McDonnell, 1994) was developed, there was an acknowledged uncertainty in the relationship between discharge volumes and TP from the C-51 West basin. This uncertainty remained when the 2002 Basin-Specific Feasibility Studies for the ECP basins were completed (Burns & McDonnell, 2002). The first basin to be examined under this Long-Term Plan project was the C-51W sub-basin. To better estimate the flow and TP loading and concentrations leaving the C-51W sub-basin, updated flow and TP data from the S-5AE and State Road 7 structures were analyzed, and a regression equation was developed. The results of this analysis indicate that the basin's flow-weighted TP mean concentration is approximately 118 ppb, about 36 percent less than the value used in the development of the Long-Term Plan. The net effect of this reduction is a lower estimate of the future TP loads entering Stormwater Treatment Area 1 East (STA-1E).

### **Influence of the Comprehensive Everglades Restoration Plan Projects on Inflow Volumes and Loads**

As the CERP projects proceed through planning and implementation, the projected impact of these projects on the inflow volumes and loads to the STAs and to receiving water bodies in the EPA needs to be updated. Of particular interest is the EAA Storage Reservoirs project, which will be linked operationally to one or more of the STAs upon its completion. During preparation of the Basin-Specific Feasibility Studies, very little information was available about the relationship of the EAA storage reservoirs outflows to STA inflows and, therefore, various assumptions were made with the understanding that future updates would be made as more information became available. Because the Phase I EAA storage reservoir has been expedited to the design phase, better information now exists regarding the proposed size, location, and operation of the reservoir, which will provide inflows to the STAs. As recommended in the Long-Term Plan, estimated inflows to the STAs will be fully readdressed following completion of the initial planning, hydrologic analyses, plan selection, and water quality change projections for the Phase I

EAA Reservoir project. This first update is scheduled to occur in FY2005. No activities were scheduled for this project in FY2004.

### **Lake Okeechobee Long-Term Trends**

Lake Okeechobee will contribute a significant portion of the water anticipated to be captured and treated in the STAs. A better understanding of the temporal and spatial characteristics of the water leaving the lake is needed for updated STA performance projections. An examination of the water quality and flow from the structures discharging lake water into the EAA (S-351, S-352, and S-354) and ultimately into the STAs is currently being conducted by the District.

### **Adaptive Implementation**

Part 6 of the Long-Term Plan includes a recommendation that to a dedicated funding source be established to facilitate the adaptive implementation process and assure that additional steps are expeditiously implemented. It was recommended that the use of this funding be limited to additional enhancements and modifications resulting from the PDE process that could be implemented within the footprints of the ECP STAs, or added to CERP projects as a locally preferred option to enhance their water quality performance. The Long-Term Plan includes a recommendation for funding of \$36 million distributed as \$9 million per year from FY2007–FY2010. Although no funds were recommended for this project until FY2007, an opportunity arose in FY2004 to integrate with the expedited Bolles and Cross Canal Improvements project with the goal of improving the ability to provide interbasin transfer of water among the STAs for more balanced and integrated operations. Excess funds that were not needed for several Long-Term Plan projects were provided to assist with the surveying phase of the Bolles and Cross Canal Improvements project. Additional information on this revision to the Long-Term Plan, including the transfer of funds and the FDEP approval of the revision, is further discussed in the *Revisions to the Long-Term Plan* section of this chapter.

### **Program Management**

During FY2004, program management activities performed by the District and contractors included maintenance of the P3E project schedules, STA operational support, and overall Everglades program coordination. In FY2004, the Operation Plans for STA-1W, STA-2, STA-3/4, STA-5, and STA-6 were updated. The initial Operation Plan for STA-1E was also developed by the District.

---

## REVISIONS TO THE LONG-TERM PLAN

---

As stated in the amended EFA (2003), revisions to the Long-Term Plan shall be incorporated through an adaptive management approach including a PDE component to identify and implement incremental optimization measures for further phosphorus reductions. Also, as stated in the amended EFA, revisions to the Long-Term Plan shall be approved by the FDEP.

The Long-Term Plan dated October 27, 2003 includes a proposed process for revisions to the plan. Revisions to the Long-Term Plan are classified as minor or major based upon the following criteria: (1) the magnitude and nature of the proposed revisions; (2) the potential for the proposed revision to have environmental impacts that are significantly different from those previously considered by the FDEP for the project; (3) the potential for the revision to adversely impact the intent and purpose of the Long-Term Plan; and (4) whether the revision requires approval by the District's governing board. As required in Section 1.10.4 of the Long-Term Plan, a description of the revision, whether minor or major, is to be included in the annual consolidated report.

On March 18, 2004, the District submitted via e-mail the first request to the FDEP for a proposed revision to the Long-Term Plan. A description of the proposed Revision 1 to the plan is presented below:

### **Revision 1 to the Long-Term Plan**

**Scope:** Consistent with the existing Plan:

To facilitate the adaptive implementation process and assure that additional steps are expeditiously implemented, the District is proposing to add a paragraph to Bc88 (Adaptive Implementation, section 6.3.1 page 6-92) describing pre-2006 activities to implement the intent of the interbasin transfer concept.

Interbasin transfer of water among the STAs for more balanced and integrated operations (Page 6-3 of the Long-term Plan).

This project will improve interbasin transfer of water among the Hillsboro, North New River and Miami Canal basins, benefiting STA-2 and STA-3/4. Also, this activity is consistent with other concepts of the existing Plan:

Enhance integration with CERP (page 5-1).

Significant technical and economic benefits can be realized by integrating Everglades water quality performance measures with CERP projects, even to the extent that existing schedules should be re-evaluated in some basins and synchronized with CERP project schedules (page 5-1).

The FY04 activity consists of assisting with the funding of the survey work in advance of design and construction of the Bolles and Cross Canal improvements. The FY05 and FY06 activities will advance the design and possibly expedite the commencement of construction of the canal improvements.

**Budget:**

\$330,000 in FY04

\$500,000 in FY05 (estimate)

\$500,000 in FY06 (estimate)

On April 15, 2004, the FDEP approved via e-mail the District's first proposed revision to the Long-Term Plan. As part of its review, the FDEP concurred that the revision constituted a minor revision, and that the Bolles and Cross Canal improvements would greatly improve the District's ability to integrate the EAA storage reservoir into STA optimization through enhanced ability for cross basin transfer of flows.

---

## **CHALLENGES TO ACHIEVING LONG-TERM WATER QUALITY GOALS**

---

Successful implementation of the Long-Term Plan will require integration of numerous research, planning, regulatory, and construction activities, as introduced in Chapter 1 of this volume. The District and the FDEP are committed to achieving these long-term water quality goals. Some of the more significant challenges for these goals include regulatory issues, uncertainties in long-term performance of source control and in regional treatment technologies, and integration with CERP projects.

### **REGULATORY ISSUES**

In July 2003, the State of Florida's Environmental Regulation Commission (ERC) adopted a phosphorus-specific water quality standard for phosphorus within the EPA that includes:

1. A numeric criterion of 10 ppb for TP in the EPA.
2. Moderating provisions which authorize discharge to the EPA where net improvement is provided in impacted areas, or where hydropattern restoration benefits clearly outweigh adverse impacts in unimpacted areas.
3. A method for determining achievement of the TP criterion.

In June 2004, an administrative law judge issued a Final Order in favor of the State of Florida supporting the ERC's adopted TP rule. The rule was then submitted to the U.S. Environmental Protection Agency (USEPA) for approval upon resolution of the challenges. Additional information on the adopted TP standard can be found in Chapter 2C of this volume.

The Long-Term Plan being implemented by the District has the planning goal of achieving water quality standards, including the TP criterion in the EPA. During the initial phase of implementation (pre-2016) of the Long-Term Plan, permits issued by the FDEP shall be based on Best Available Phosphorus Reduction Technology, as defined by the EFA, and shall include Technology-Based Effluent Limits consistent with the Long-Term Plan.

In addition, the FDEP must evaluate water quality standards for parameters other than TP for the EPA and EAA canals. As a part of this evaluation, the FDEP is also specifically directed by the EFA to recognize by rulemaking the existing beneficial uses of the EAA conveyance canals. Although the EFA does not set a specific deadline for this rulemaking, it is assumed that it will be completed by December 31, 2006. Other regulatory issues are discussed in Chapter 3 of this volume.

## **STORMWATER TREATMENT AREA OPTIMIZATION RESEARCH**

Chapter 4 of this volume presents a summary of STA optimization research which occurred in FY2004. While critical research is continuing on STA optimization, the Long-Term Plan includes a process of adaptive implementation to incorporate the best available and scientifically defensible information during implementation of the Long-Term Plan.

## **SOURCE CONTROL MEASURES**

While landowners within the EAA as a whole have implemented effective source control BMPs, the Long-Term Plan includes funding for identification of “hot spots” within the EAA, and for implementation of source control measures in these locations. The Long-Term Plan also includes funding for identification and implementation of source control measures in other rural (non-ECP) basins and in urban basins. Compared to what is known about source control measures in the EAA, minimal information is currently known about the technical efficacy and economics of controlling TP loads from the non-ECP basins (i.e., urban and non-EAA basins). Controlling TP loads at the source, both in the EAA and the non-ECP basins, is a high priority in the Long-Term Plan. For this reason, source control development and implementation funding was provided in FY2004, and will continue to be provided throughout the implementation of the Long-Term Plan.

## **SYNCHRONIZATION WITH COMPREHENSIVE EVERGLADES RESTORATION PLAN PROJECTS**

The majority of Everglades tributary basins contain proposed CERP projects. During FY2004, the District coordinated with members of CERP’s PDTs in an effort to integrate Long-Term Plan projects with CERP projects, where possible, consistent with the following language from the amended EFA:

It is the intent of the Legislature that implementation of the Long-Term Plan shall be integrated and consistent with the implementation of the projects and activities in the Congressionally authorized components of the CERP so that unnecessary and duplicative costs will be avoided. Nothing in this section shall modify any existing cost share or responsibility provided for projects listed in s. 528 of the Water Resources Development Act of 1996 (110 Stat. 3769) or provided for projects listed in section 601 of the Water Resources Development Act of 2000 (114 Stat. 2572). The Legislature does not intend for the provisions of this section to diminish commitments made by the State of Florida to restore and maintain water quality in the Everglades Protection Area, including the federal lands in the settlement agreement referenced in paragraph (4)(e).

Integration efforts in FY2004 generally consisted of providing funds from Long-Term Plan projects to CERP projects for activities such as analysis of potential water quality improvement features that could be added to CERP projects as locally preferred options. In the case of the first approved minor revision to the Long-Term Plan, the integration effort consisted of providing excess funds from several Long-Term Plan projects to a CERP project that, upon completion, will allow improved water quality improvement performance for the ECP. The potential remains for significant cost savings by integrating some of the Long-Term Plan components with CERP projects. Many of the CERP projects are still in the early planning and design phases. Therefore, uncertainty continues to exist in how CERP projects will influence flows and water quality as well as their implementation schedules. Continued close coordination is needed between

members of the PDTs and staff implementing the Long-Term Plan components to ensure that project goals are met on schedule.

---

## CONCLUSIONS

---

The Long-Term Plan is predicated upon maximizing water quality improvement through an adaptive implementation process in which:

- All scientifically defensible steps are taken at the earliest achievable dates and in full recognition of the timeline established in the EFA.
- Focused efforts are directed to improving the scientific and technical basis for additional steps, leading to incremental implementation of those steps as soon as their needs are confirmed.
- The synergy between this effort and other regional efforts, particularly CERP, is recognized, and maximum benefit realized from full integration with those efforts.
- Existing and proposed treatment facilities are operated, maintained, and monitored to maximize their treatment effectiveness.
- Steps are being taken to accelerate the recovery of previously impacted areas in the EPA, including completion of the hydropattern restoration goals of the EFA.

The District is actively implementing the numerous projects of the Long-Term Plan, as required by the EFA, and is following a process of adaptive implementation consistent with the above-mentioned goals and objectives.

---

## LITERATURE CITED

---

- Brown & Caldwell. 2002. Basin Specific Feasibility Studies for the Everglades Stormwater Program Basins. October 2002. Report prepared for the South Florida Water Management District, West Palm Beach, FL.
- Burns & McDonnell. 1994. Everglades Protection Project Conceptual Design. February 1994. Report prepared for the South Florida Water Management District, West Palm Beach, FL.
- Burns & McDonnell. 2002. Evaluation of Alternatives for the ECP Basins. October 2002. Report prepared for the South Florida Water Management District, West Palm Beach, FL.
- Burns & McDonnell. 2003. Everglades Protection Area Tributary Basins Long-Term Plan for Achieving Water Quality Goals. October 2003. Report prepared for the South Florida Water Management District, West Palm Beach, FL.
- Goforth, G. and T. Piccone. 2001. Baseline Data for the Basin-Specific Feasibility Studies to Achieve the Long-Term Water Quality Goals for the Everglades. South Florida Water Management District, West Palm Beach, FL.
- Walker, W.W. and R.H. Kadlec. 2002. Development of a Dynamic Model for Stormwater Treatment Areas. Report and Model prepared for the U.S. Department of the Interior.
